



Ocala Florida
Entitlements Schedule

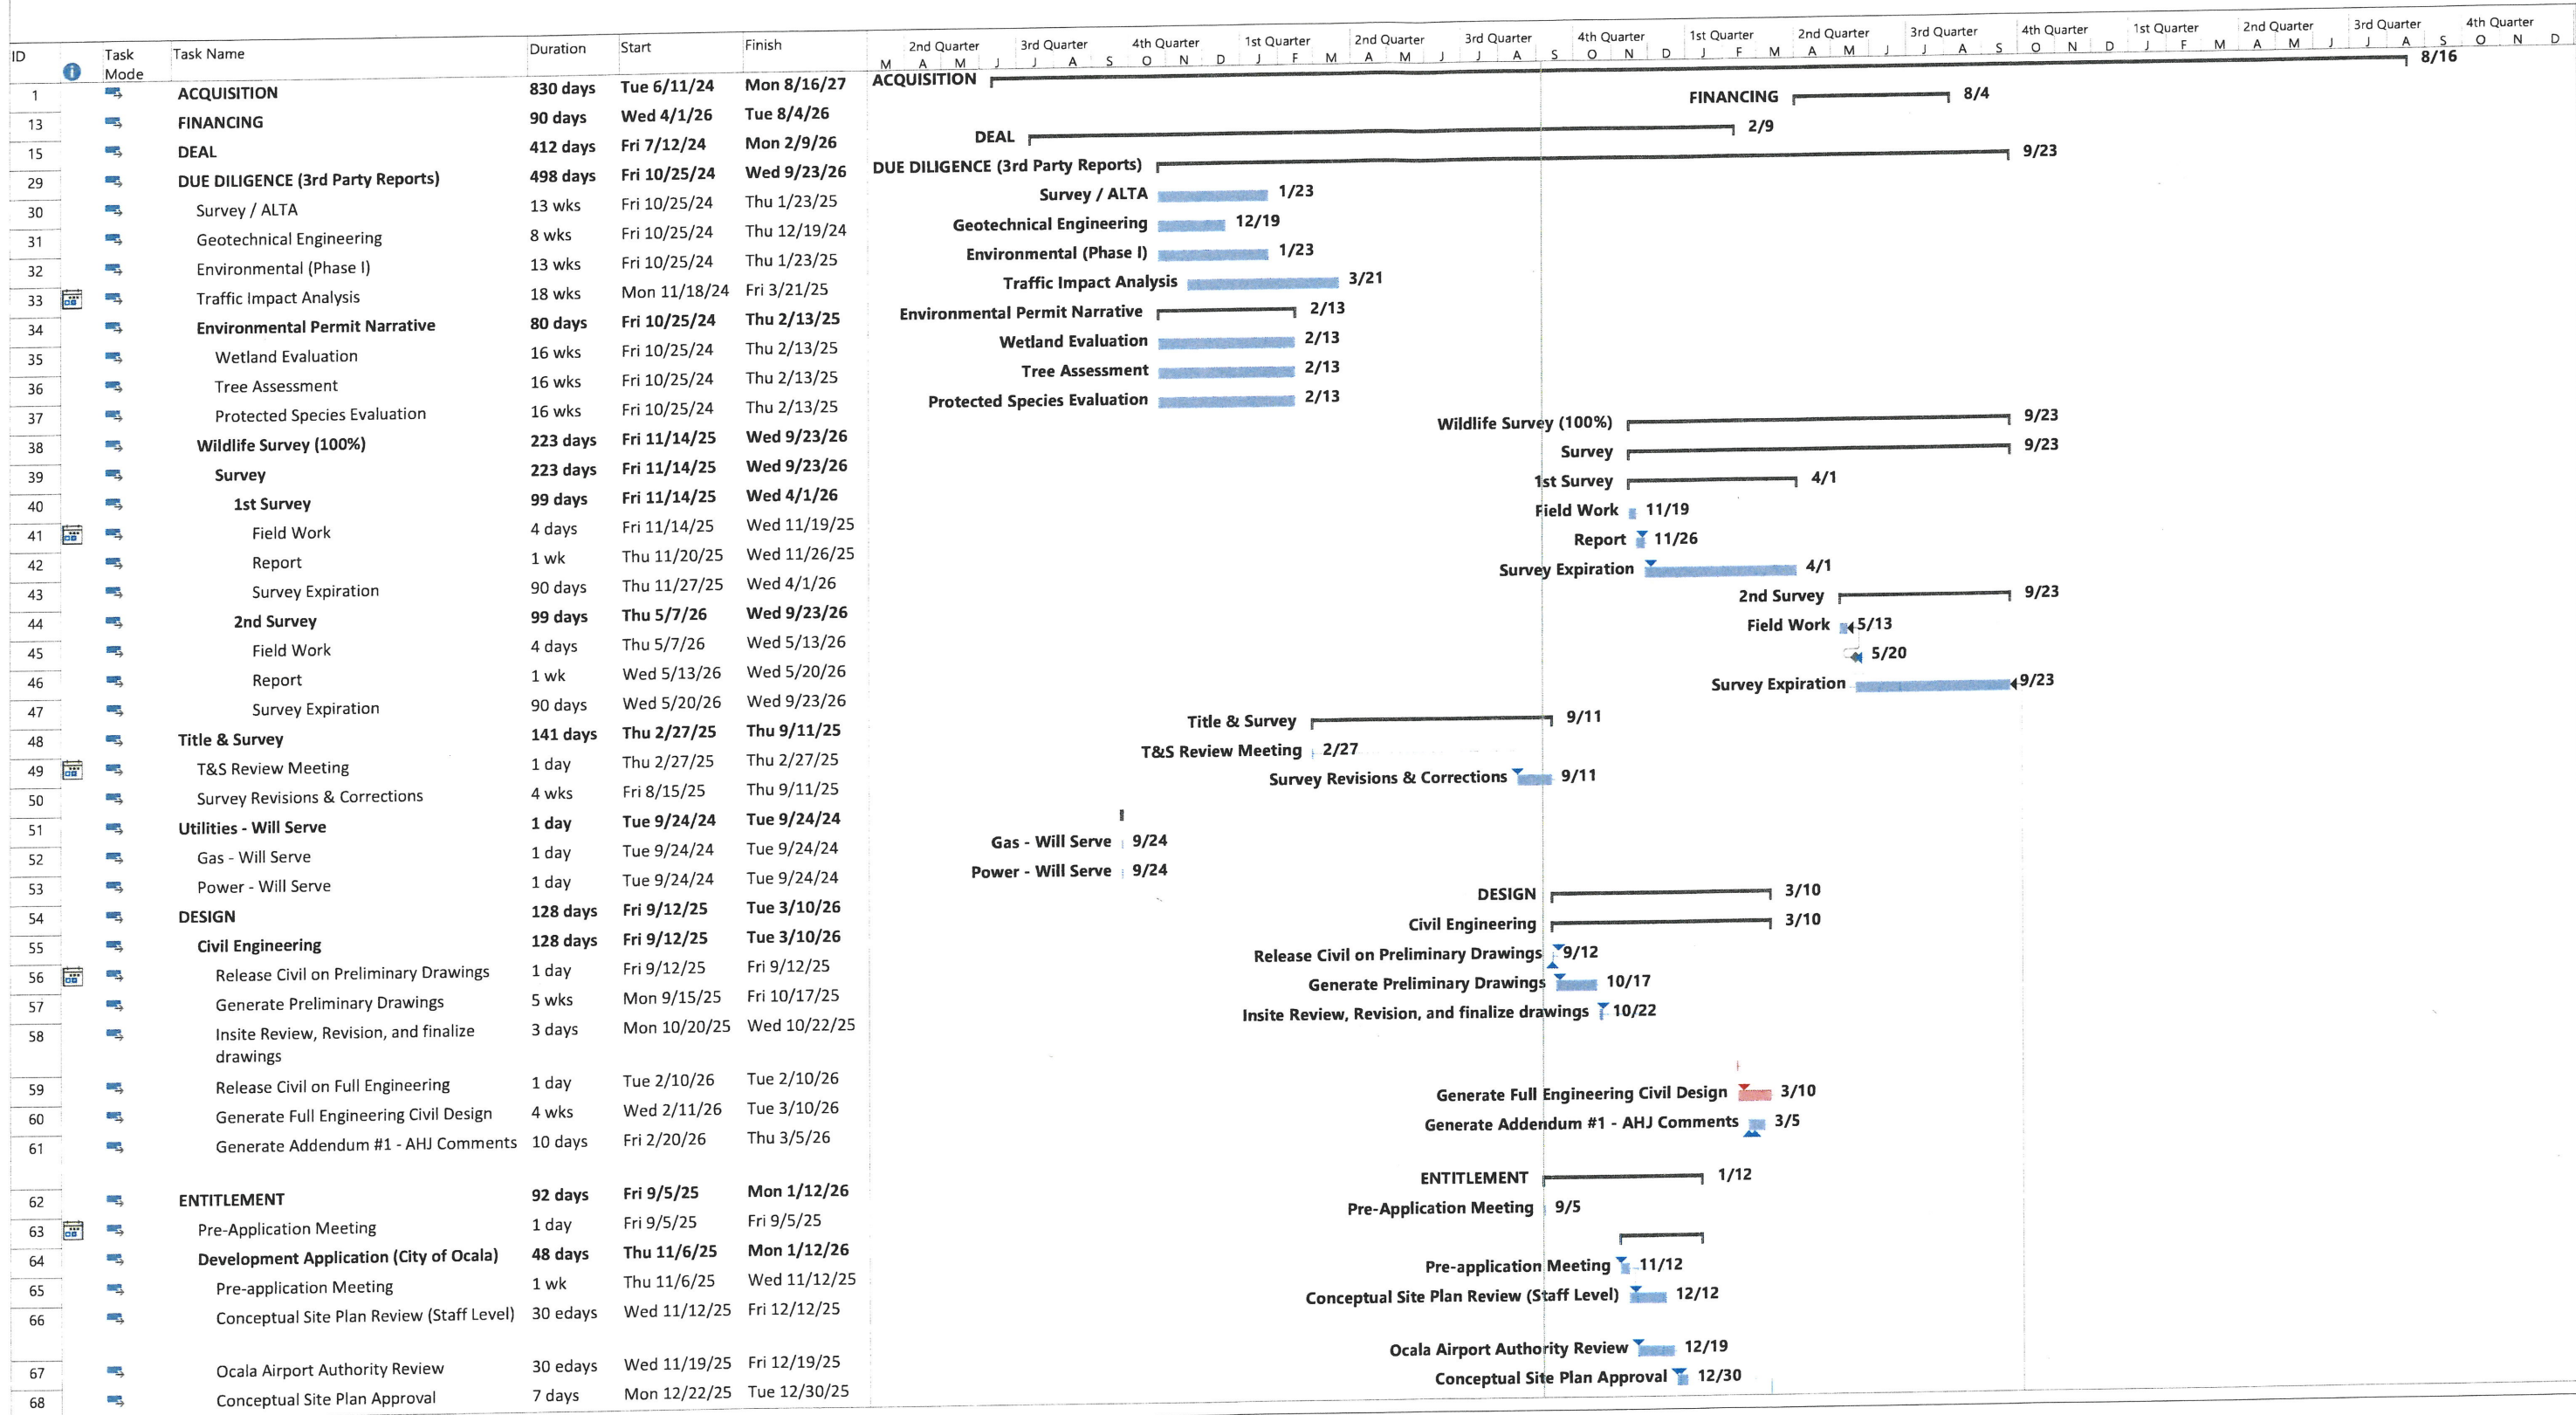

Project: 20250905-OcalaFL_Sch
Date: Fri 9/5/25

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

Ocala Florida
Entitlements Schedule

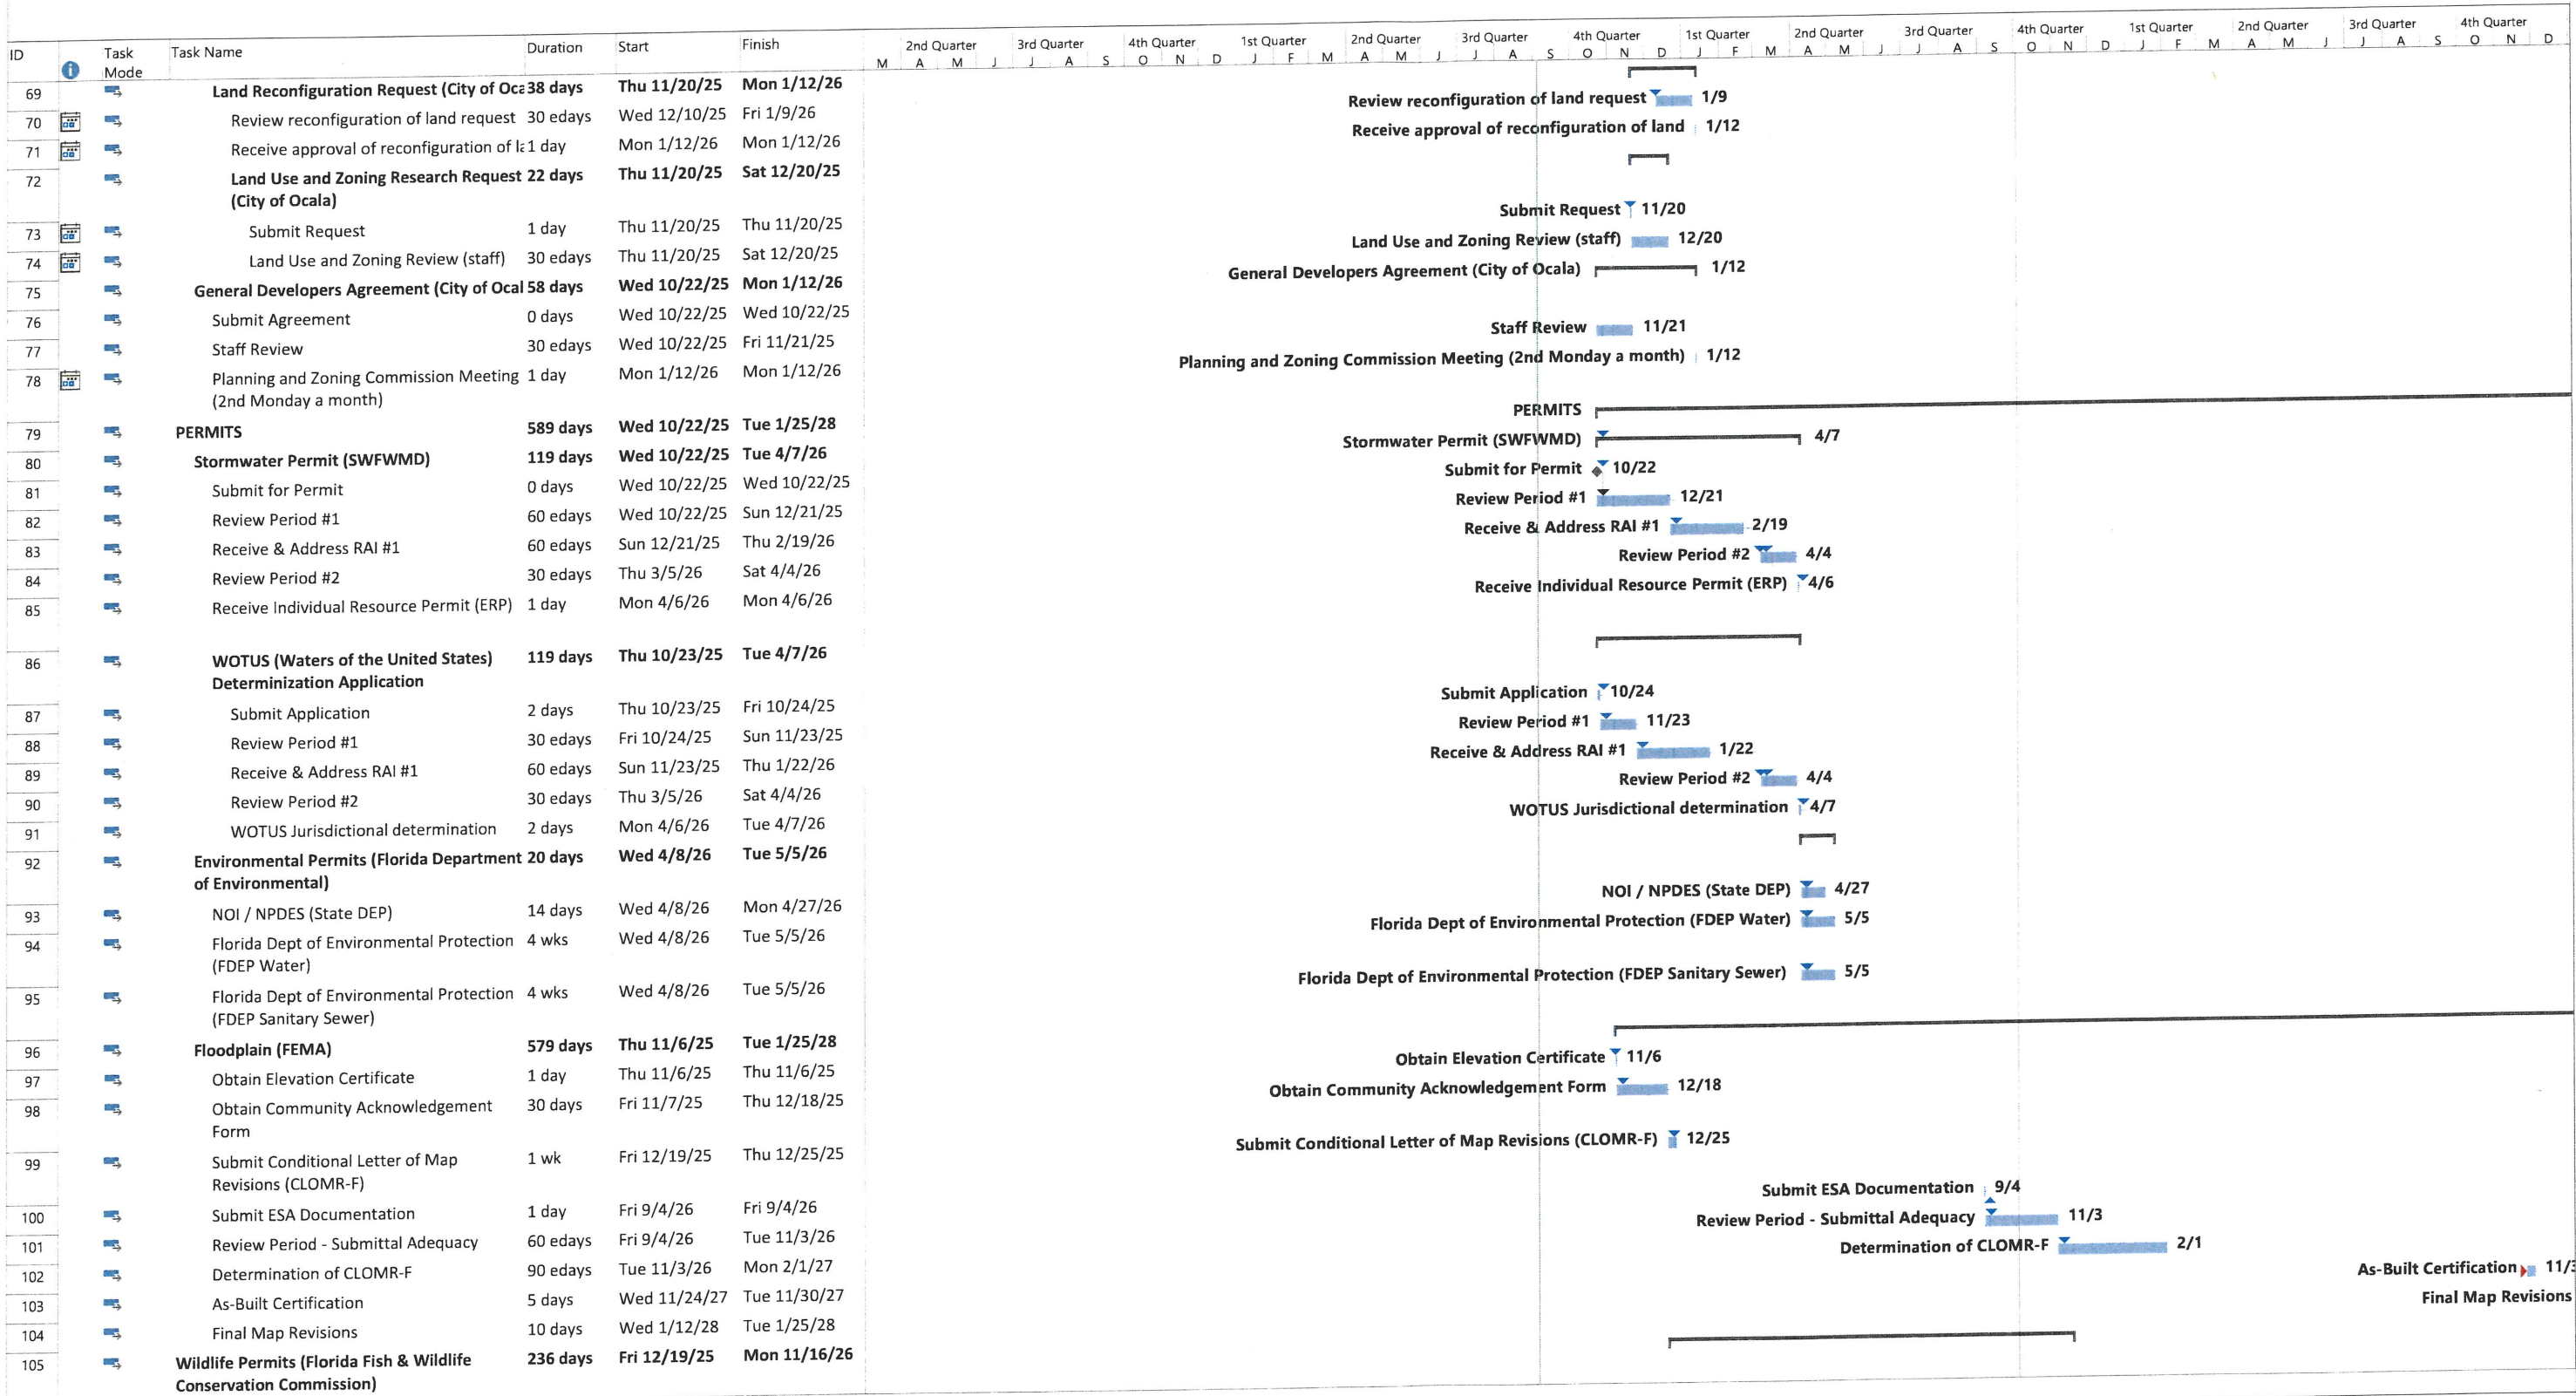

Project: 2025109010 OcalaFL_Sch
Date: Fri 9/5/25

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

Entitlements Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	
106		Gopher Turtles	77 days	Wed 5/20/26	Thu 9/3/26	
107		Apply for Gopher Turtle Relocation Permit	7 days	Wed 5/20/26	Thu 5/28/26	Apply for Gopher Turtle Relocation Permit 5/28
108		Apply for Gopher Turtle Recipient Site Permit	7 days	Wed 5/20/26	Thu 5/28/26	Apply for Gopher Turtle Recipient Site Permit 5/28
109		Permit Review Period	60 edays	Thu 5/28/26	Mon 7/27/26	Permit Review Period 7/27
110		Mitigation Contributions	30 edays	Mon 7/27/26	Wed 8/26/26	Mitigation Contributions 8/26
111		Receive Gopher Turtle Relocation Permit	1 day	Thu 9/3/26	Thu 9/3/26	Receive Gopher Turtle Relocation Permit 9/3
112		Receive Gopher Turtle Recipient Site Permit	1 day	Thu 9/3/26	Thu 9/3/26	Receive Gopher Turtle Recipient Site Permit 9/3
113		Borrowing Owls	103 days	Thu 6/25/26	Mon 11/16/26	
114		Scoping of owl burrows	4 wks	Thu 6/25/26	Wed 7/22/26	Scoping of owl burrows 7/22
115		Submit Burrowing Owl observations (FWC)	1 wk	Thu 7/30/26	Wed 8/5/26	Submit Burrowing Owl observations (FWC) 8/5
116		Apply for Burrowing Owl incidental Take Permit (FWC)	1 day	Thu 8/6/26	Thu 8/6/26	Apply for Burrowing Owl incidental Take Permit (FWC) 8/6
117		Borrowing Owl Permit Review	60 edays	Thu 8/6/26	Mon 10/5/26	Borrowing Owl Permit Review 10/5
118		FWC Request for Additional Information (RAI)	10 edays	Mon 10/5/26	Thu 10/15/26	FWC Request for Additional Information (RAI) 10/15
119		Submit RAI to FWC	1 day	Fri 10/16/26	Fri 10/16/26	Submit RAI to FWC 10/16
120		FWC review of RAI Responses	30 edays	Fri 10/16/26	Sun 11/15/26	FWC review of RAI Responses 11/15
121		Issuance of Burrowing Owl take permit	1 day	Mon 11/16/26	Mon 11/16/26	Issuance of Burrowing Owl take permit 11/16
122		Development Permit (City of Ocala)	41 days	Wed 3/11/26	Wed 5/6/26	
123		Construction Plan improvements (12 months conceptual plan approval) submittal	19 days	Wed 3/11/26	Mon 4/6/26	Construction Plan improvements (12 months conceptual plan approval) submittal 4/6
124		Planning and Zoning Commission Meeting (2nd Monday a month)	1 day	Tue 4/7/26	Tue 4/7/26	Planning and Zoning Commission Meeting (2nd Monday a month) 4/7
125		Development Permit Approval	5 days	Wed 4/15/26	Tue 4/21/26	Development Permit Approval 4/21
126		Final Plat submittal	1 day	Wed 5/6/26	Wed 5/6/26	Final Plat submittal 5/6
127		Tree Removal (City of Ocala)	39 days	Wed 3/11/26	Mon 5/4/26	
128		Complete Tree Restoration Plan	5 days	Wed 3/11/26	Tue 3/17/26	Complete Tree Restoration Plan 3/17
129		Submit Tree Removal Plan Application	2 days	Wed 3/18/26	Thu 3/19/26	Submit Tree Removal Plan Application 3/19
130		Tree Removal Permit Review	30 days	Fri 3/20/26	Thu 4/30/26	Tree Removal Permit Review 4/30
131		Receive Tree removal Permit	2 days	Fri 5/1/26	Mon 5/4/26	Receive Tree removal Permit 5/4
132		Driveway Permit (City of Ocala)	39 days	Wed 3/11/26	Mon 5/4/26	
133		Submit Application for Driveway Permit	2 days	Wed 3/11/26	Thu 3/12/26	Submit Application for Driveway Permit 3/12
134		Permit Application Review	30 days	Fri 3/13/26	Thu 4/23/26	Permit Application Review 4/23
135		Receive Driveway Permit	2 days	Fri 5/1/26	Mon 5/4/26	Receive Driveway Permit 5/4
136		Building Permit (City of Ocala)	52 days	Wed 4/22/26	Thu 7/2/26	
137		Submit Building Permit Application	1 wk	Wed 4/22/26	Tue 4/28/26	Submit Building Permit Application 4/28
138		Building Department Review	8 wks	Wed 4/29/26	Tue 6/23/26	Building Department Review 6/23
139		Receive Building Permit	1 day	Thu 7/2/26	Thu 7/2/26	Receive Building Permit 7/2
140		Ocala Airport Authority	133 days	Fri 12/19/25	Wed 6/24/26	
141		Submit Plans for Airport Review	2 days	Wed 4/29/26	Thu 4/30/26	Submit Plans for Airport Review 4/30

Ocala Florida Entitlements Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		3rd Quarter		4th Quarter		1st Quarter		2nd Quarter		3rd Quarter		4th Quarter	
						M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
142		FAA Obstruction Analysis	90 edays	Fri 12/19/25	Thu 3/19/26	FAA Obstruction Analysis										3/19											
143		Final Approval from Ocala Airport	1 day	Wed 6/24/26	Wed 6/24/26	Final Approval from Ocala Airport										6/24											
144		WILDLIFE MITIGATION/REMOVAL	172 days	Wed 5/20/26	Thu 1/14/27	WILDLIFE MITIGATION/REMOVAL										1/14											
145		Gopher Tortoises (FWC) (Removal Seasons - April 1 - October 15)	78 days	Wed 5/20/26	Fri 9/4/26	Gopher Tortoises (FWC) (Removal Seasons - April 1 - October 15)										9/4											
146		24 hour notice to FWC	1 day	Fri 9/4/26	Fri 9/4/26	24 hour notice to FWC										9/4											
147		Preparation of recipient site	14 edays	Wed 5/20/26	Wed 6/3/26	Preparation of recipient site										6/3											
148		Inspection and Removal of Nests (May - September 15)	14 edays	Wed 6/3/26	Wed 6/17/26	Inspection and Removal of Nests (May - September 15)										6/17											
149		Examination of Burrow	14 edays	Wed 6/3/26	Wed 6/17/26	Examination of Burrow										6/17											
150		Capture of Tortoises	30 days	Wed 6/17/26	Tue 7/28/26	Capture of Tortoises										7/28											
151		Holding of Tortoises (24hour Max)	1 day	Thu 6/18/26	Thu 6/18/26	Holding of Tortoises (24hour Max)										6/18											
152		Preparation for transportation	1 day	Fri 6/19/26	Fri 6/19/26	Preparation for transportation										6/19											
153		Transportation	1 day	Thu 6/18/26	Thu 6/18/26	Transportation										6/18											
154		Release	5 days	Thu 6/18/26	Wed 6/24/26	Release										6/24											
155		Submit permitting reports	10 days	Thu 8/6/26	Wed 8/19/26	Submit permitting reports										8/19											
156		Burrowing Owl (FWC) (Nesting Season - July 11th to February 14th)	43 days	Tue 11/17/26	Thu 1/14/27	Burrowing Owl (FWC) (Nesting Season - July 11th to February 14th)										11/30											
157		Scoping & Collapsing of burrows	10 days	Tue 11/17/26	Mon 11/30/26	Scoping & Collapsing of burrows										11/30											
158		Submit Permitting reports	3 days	Tue 12/1/26	Thu 12/3/26	Submit Permitting reports										12/3											
159		FWC Verification of completeness	30 days	Fri 12/4/26	Thu 1/14/27	FWC Verification of completeness										1/14											
160		UTILITIES/EASEMENTS	165 days	Wed 3/11/26	Tue 10/27/26	UTILITIES/EASEMENTS										10/27											
161		Power	165 days	Wed 3/11/26	Tue 10/27/26	Power										10/27											
162		Service Extension	165 days	Wed 3/11/26	Tue 10/27/26	Service Extension										10/27											
163		Agreement	45 days	Wed 3/11/26	Tue 5/12/26	Agreement										5/12											
164		Extension	6 mons	Wed 5/13/26	Tue 10/27/26	Extension										5/12											
165		Power - Easement Agreement & Depictions / Exhibits	45 days	Wed 3/11/26	Tue 5/12/26	Power - Easement Agreement & Depictions / Exhibits										5/12											
166		Telecom - Easement Agreement & Depictions / Exhibits	45 days	Wed 3/11/26	Tue 5/12/26	Telecom - Easement Agreement & Depictions / Exhibits										5/12											
167		PROCUREMENT (General Contractor)	178 days	Fri 2/20/26	Wed 10/28/26	PROCUREMENT (General Contractor)										10/28											
168		Prepare RFP	3 days	Fri 2/20/26	Tue 2/24/26	Prepare RFP										2/24											
169		Bidding	15 days	Wed 2/25/26	Tue 3/17/26	Bidding										3/17											
170		Receive Proposals	0 days	Tue 3/17/26	Tue 3/17/26	Receive Proposals										3/17											
171		Level Proposals	10 days	Wed 3/18/26	Tue 3/31/26	Level Proposals										3/31											
172		Issue LOI	0 days	Tue 3/31/26	Tue 3/31/26	Issue LOI										3/31											
173		Draft / Execute Contract	5 days	Wed 4/1/26	Tue 4/7/26	Draft / Execute Contract										4/7											
174		Notice of Commencement	45 edays	Sun 9/13/26	Wed 10/28/26	Notice of Commencement										10/28											
175		CONSTRUCTION	370 days	Wed 10/28/26	Tue 3/28/28	CONSTRUCTION										11/10											
176		Mobilize	10 days	Wed 10/28/26	Tue 11/10/26	Mobilize										11/10											
177		Construction Cycle	18 mons	Wed 11/11/26	Tue 3/28/28	Construction Cycle										Substantial											
178		Tenant Access - Fixturing	60 days	Mon 11/8/27	Fri 1/28/28	Tenant Access - Fixturing										Substantial											
179		Substantial Completion	0 days	Tue 3/28/28	Tue 3/28/28	Substantial Completion										Substantial											
