



Ocala Florida  
Entitlements Schedule

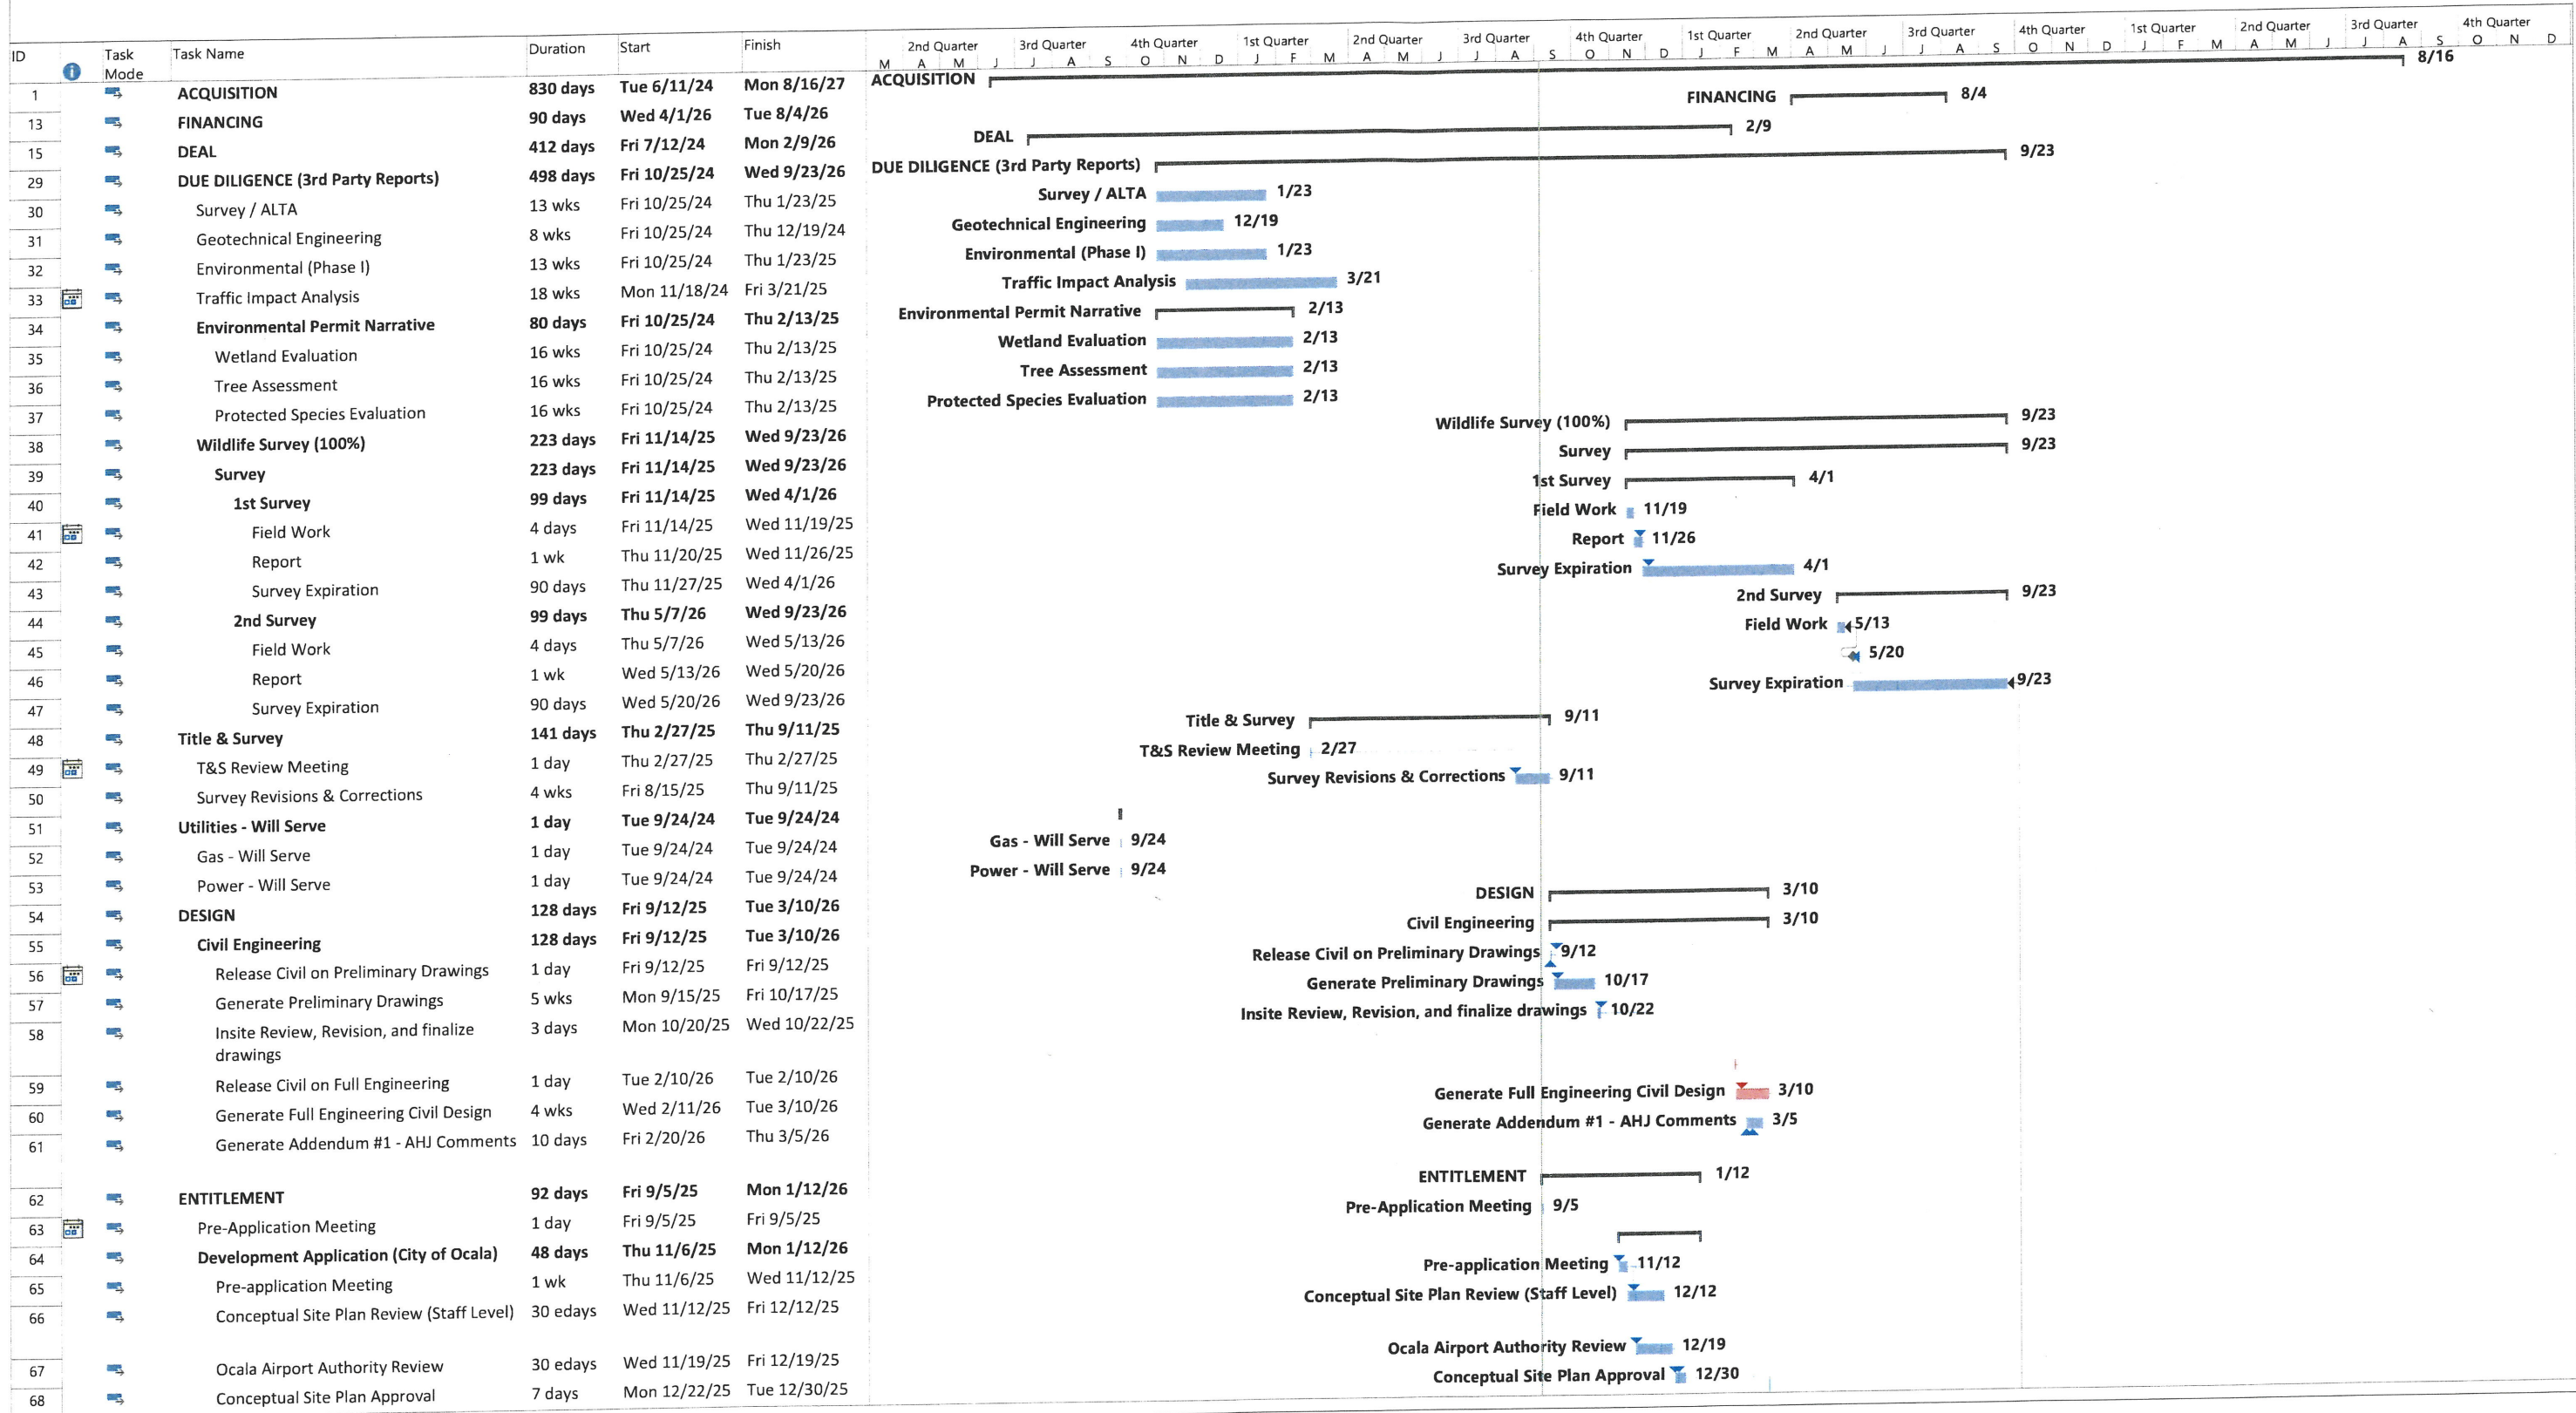

Project: 20250905-OcalaFL\_Sch  
Date: Fri 9/5/25

|           |                 |                    |                       |                |                    |                 |
|-----------|-----------------|--------------------|-----------------------|----------------|--------------------|-----------------|
| Task      | Summary         | Inactive Milestone | Duration-only         | Start-only     | External Milestone | Critical Split  |
| Split     | Project Summary | Inactive Summary   | Manual Summary Rollup | Finish-only    | Deadline           | Progress        |
| Milestone | Inactive Task   | Manual Task        | Manual Summary        | External Tasks | Critical           | Manual Progress |

Ocala Florida  
Entitlements Schedule

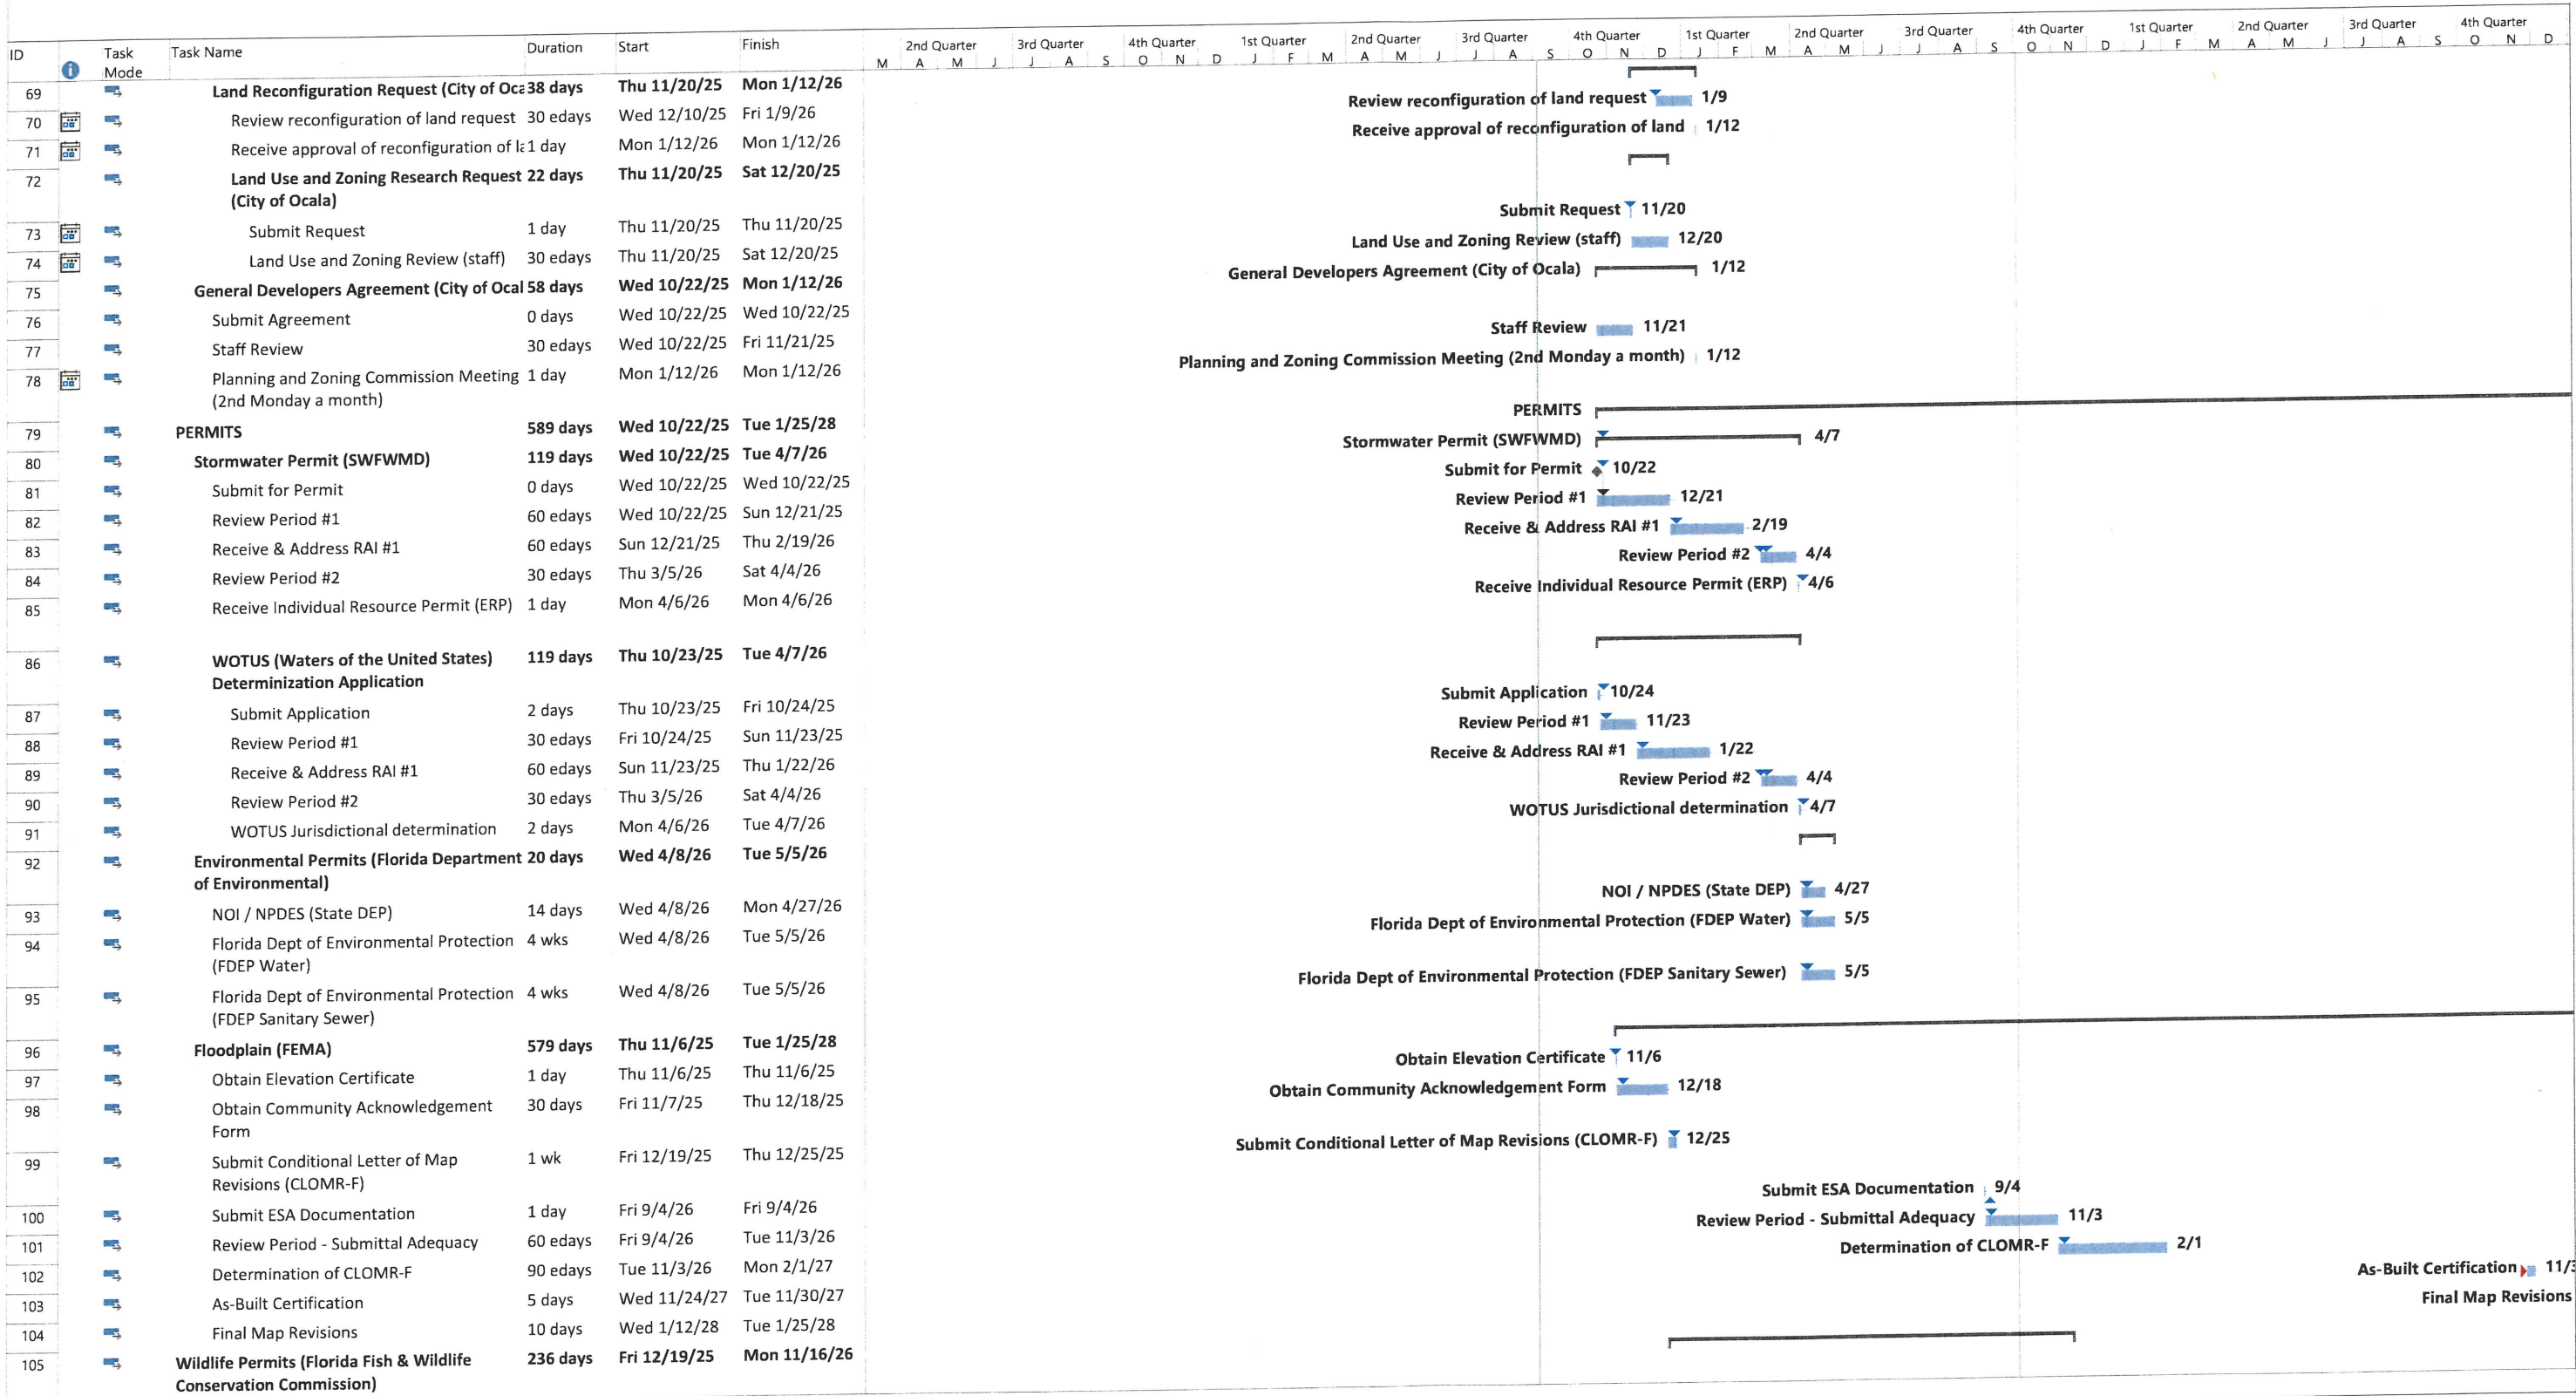

Project: 2025109010 OcalaFL\_Sch  
Date: Fri 9/5/25

|           |                 |                    |                       |                |                    |                 |
|-----------|-----------------|--------------------|-----------------------|----------------|--------------------|-----------------|
| Task      | Summary         | Inactive Milestone | Duration-only         | Start-only     | External Milestone | Critical Split  |
| Split     | Project Summary | Inactive Summary   | Manual Summary Rollup | Finish-only    | Deadline           | Progress        |
| Milestone | Inactive Task   | Manual Task        | Manual Summary        | External Tasks | Critical           | Manual Progress |

## Entitlements Schedule

| ID  | Task Mode | Task Name                                                                     | Duration | Start        | Finish       | 2nd Quarter                                                                        |   | 3rd Quarter |   | 4th Quarter |   | 1st Quarter |   | 2nd Quarter |   | 3rd Quarter |   | 4th Quarter |   | 1st Quarter |   | 2nd Quarter |   | 3rd Quarter |   | 4th Quarter |   | 1st Quarter |   | 2nd Quarter |   | 3rd Quarter |   | 4th Quarter |   |   |   |   |   |
|-----|-----------|-------------------------------------------------------------------------------|----------|--------------|--------------|------------------------------------------------------------------------------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|-------------|---|---|---|---|---|
|     |           |                                                                               |          |              |              | M                                                                                  | A | M           | J | J           | A | S           | O | N           | D | J           | F | M           | A | M           | J | J           | A | S           | O | N           | D | J           | F | M           | A | M           | J | J           | A | S | O | N | D |
| 106 |           | Gopher Tortoises                                                              | 77 days  | Wed 5/20/26  | Thu 9/3/26   | Apply for Gopher Tortoise Relocation Permit  5/28                                  |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 107 |           | Apply for Gopher Tortoise Relocation Permit                                   | 7 days   | Wed 5/20/26  | Thu 5/28/26  | Apply for Gopher Tortoise Recipient Site Permit  5/28                              |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 108 |           | Apply for Gopher Tortoise Recipient Site Permit                               | 7 days   | Wed 5/20/26  | Thu 5/28/26  | Permit Review Period  7/27                                                         |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 109 |           | Permit Review Period                                                          | 60 edays | Thu 5/28/26  | Mon 7/27/26  | Mitigation Contributions  8/26                                                     |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 110 |           | Mitigation Contributions                                                      | 30 edays | Mon 7/27/26  | Wed 8/26/26  | Receive Gopher Tortoise Relocation Permit  9/3                                     |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 111 |           | Receive Gopher Tortoise Relocation Permit                                     | 1 day    | Thu 9/3/26   | Thu 9/3/26   | Receive Gopher Tortoise Recipient Site Permit  9/3                                 |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 112 |           | Receive Gopher Tortoise Recipient Site Permit                                 | 1 day    | Thu 9/3/26   | Thu 9/3/26   |                                                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 113 |           | Borrowing Owls                                                                | 103 days | Thu 6/25/26  | Mon 11/16/26 | Scoping of owl burrows  7/22                                                       |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 114 |           | Scoping of owl burrows                                                        | 4 wks    | Thu 6/25/26  | Wed 7/22/26  | Submit Burrowing Owl observations (FWC)  8/5                                       |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 115 |           | Submit Burrowing Owl observations (FWC)                                       | 1 wk     | Thu 7/30/26  | Wed 8/5/26   | Apply for Burrowing Owl incidental Take Permit (FWC)  8/6                          |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 116 |           | Apply for Burrowing Owl incidental Take Permit (FWC)                          | 1 day    | Thu 8/6/26   | Thu 8/6/26   | Borrowing Owl Permit Review  10/5                                                  |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 117 |           | Borrowing Owl Permit Review                                                   | 60 edays | Thu 8/6/26   | Mon 10/5/26  | FWC Request for Additional Information (RAI)  10/15                                |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 118 |           | FWC Request for Additional Information (RAI)                                  | 10 edays | Mon 10/5/26  | Thu 10/15/26 | Submit RAI to FWC  10/16                                                           |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 119 |           | Submit RAI to FWC                                                             | 1 day    | Fri 10/16/26 | Fri 10/16/26 | FWC review of RAI Responses  11/15                                                 |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 120 |           | FWC review of RAI Responses                                                   | 30 edays | Fri 10/16/26 | Sun 11/15/26 | Issuance of Burrowing Owl take permit  11/16                                       |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 121 |           | Issuance of Burrowing Owl take permit                                         | 1 day    | Mon 11/16/26 | Mon 11/16/26 | Construction Plan improvements (12 months conceptual plan approval) submittal  4/6 |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 122 |           | Development Permit (City of Ocala)                                            | 41 days  | Wed 3/11/26  | Wed 5/6/26   | Planning and Zoning Commission Meeting (2nd Monday a month)  4/7                   |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 123 |           | Construction Plan improvements (12 months conceptual plan approval) submittal | 19 days  | Wed 3/11/26  | Mon 4/6/26   | Development Permit Approval  4/21                                                  |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 124 |           | Planning and Zoning Commission Meeting (2nd Monday a month)                   | 1 day    | Tue 4/7/26   | Tue 4/7/26   | Final Plat submittal  5/6                                                          |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 125 |           | Development Permit Approval                                                   | 5 days   | Wed 4/15/26  | Tue 4/21/26  | Complete Tree Restoration Plan  3/17                                               |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 126 |           | Final Plat submittal                                                          | 1 day    | Wed 5/6/26   | Wed 5/6/26   | Submit Tree Removal Plan Application  3/19                                         |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 127 |           | Tree Removal (City of Ocala)                                                  | 39 days  | Wed 3/11/26  | Mon 5/4/26   | Tree Removal Permit Review  4/30                                                   |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 128 |           | Complete Tree Restoration Plan                                                | 5 days   | Wed 3/11/26  | Tue 3/17/26  | Receive Tree removal Permit  5/4                                                   |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 129 |           | Submit Tree Removal Plan Application                                          | 2 days   | Wed 3/18/26  | Thu 3/19/26  | Submit Application for Driveway Permit  3/12                                       |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 130 |           | Tree Removal Permit Review                                                    | 30 days  | Fri 3/20/26  | Thu 4/30/26  | Permit Application Review  4/23                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 131 |           | Receive Tree removal Permit                                                   | 2 days   | Fri 5/1/26   | Mon 5/4/26   | Receive Driveway Permit  5/4                                                       |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 132 |           | Driveway Permit (City of Ocala)                                               | 39 days  | Wed 3/11/26  | Mon 5/4/26   | Submit Building Permit Application  4/28                                           |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 133 |           | Submit Application for Driveway Permit                                        | 2 days   | Wed 3/11/26  | Thu 3/12/26  | Building Department Review  6/23                                                   |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 134 |           | Permit Application Review                                                     | 30 days  | Fri 3/13/26  | Thu 4/23/26  | Receive Building Permit  7/2                                                       |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 135 |           | Receive Driveway Permit                                                       | 2 days   | Fri 5/1/26   | Mon 5/4/26   | Submit Plans for Airport Review  4/30                                              |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 136 |           | Building Permit (City of Ocala)                                               | 52 days  | Wed 4/22/26  | Thu 7/2/26   |                                                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 137 |           | Submit Building Permit Application                                            | 1 wk     | Wed 4/22/26  | Tue 4/28/26  |                                                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 138 |           | Building Department Review                                                    | 8 wks    | Wed 4/29/26  | Tue 6/23/26  |                                                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 139 |           | Receive Building Permit                                                       | 1 day    | Thu 7/2/26   | Thu 7/2/26   |                                                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 140 |           | Ocala Airport Authority                                                       | 133 days | Fri 12/19/25 | Wed 6/24/26  |                                                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |
| 141 |           | Submit Plans for Airport Review                                               | 2 days   | Wed 4/29/26  | Thu 4/30/26  |                                                                                    |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |             |   |   |   |   |   |

## Ocala Florida Entitlements Schedule

| ID  | Task Mode | Task Name                                                         | Duration | Start        | Finish       | 2026                                                      |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
|-----|-----------|-------------------------------------------------------------------|----------|--------------|--------------|-----------------------------------------------------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|-------------|---|---|---|---|---|--|--|--|--|--|--|
|     |           |                                                                   |          |              |              | 2nd Quarter                                               |   |   |   | 3rd Quarter |   |   |   | 4th Quarter |   |   |   | 1st Quarter |   |   |   | 2nd Quarter |   |   |   | 3rd Quarter |   |   |   | 4th Quarter |   |   |   | 1st Quarter |   |   |   | 2nd Quarter |   |   |   | 3rd Quarter |   |   |   | 4th Quarter |   |   |   |   |   |  |  |  |  |  |  |
|     |           |                                                                   |          |              |              | M                                                         | A | M | J | J           | A | S | O | N           | D | J | F | M           | A | M | J | J           | A | S | O | N           | D | J | F | M           | A | M | J | J           | A | S | O | N           | D | J | F | M           | A | M | J | J           | A | S | O | N | D |  |  |  |  |  |  |
| 142 |           | FAA Obstruction Analysis                                          | 90 edays | Fri 12/19/25 | Thu 3/19/26  | FAA Obstruction Analysis 3/19                             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 143 |           | Final Approval from Ocala Airport                                 | 1 day    | Wed 6/24/26  | Wed 6/24/26  | Final Approval from Ocala Airport 6/24                    |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 144 |           | WILDLIFE MITIGATION/REMOVAL                                       | 172 days | Wed 5/20/26  | Thu 1/14/27  | WILDLIFE MITIGATION/REMOVAL 1/14                          |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 145 |           | Gopher Tortoises (FWC) (Removal Seasons - April 1 - October 15)   | 78 days  | Wed 5/20/26  | Fri 9/4/26   | 24 hour notice to FWC 9/4                                 |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 146 |           | 24 hour notice to FWC                                             | 1 day    | Fri 9/4/26   | Fri 9/4/26   | Preparation of recipient site 6/3                         |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 147 |           | Preparation of recipient site                                     | 14 edays | Wed 5/20/26  | Wed 6/3/26   | Inspection and Removal of Nests (May - September 15) 6/17 |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 148 |           | Inspection and Removal of Nests (May - September 15)              | 14 edays | Wed 6/3/26   | Wed 6/17/26  | Examination of Burrow 6/17                                |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 149 |           | Examination of Burrow                                             | 14 edays | Wed 6/3/26   | Wed 6/17/26  | Capture of Tortoises 7/28                                 |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 150 |           | Capture of Tortoises                                              | 30 days  | Wed 6/17/26  | Tue 7/28/26  | Holding of Tortoises (24hour Max) 6/18                    |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 151 |           | Holding of Tortoises (24hour Max)                                 | 1 day    | Thu 6/18/26  | Thu 6/18/26  | Preparation for transportation 6/19                       |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 152 |           | Preparation for transportation                                    | 1 day    | Fri 6/19/26  | Fri 6/19/26  | Transportation 6/18                                       |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 153 |           | Transportation                                                    | 1 day    | Thu 6/18/26  | Thu 6/18/26  | Release 6/24                                              |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 154 |           | Release                                                           | 5 days   | Thu 6/18/26  | Wed 6/24/26  | Submit permitting reports 8/19                            |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 155 |           | Submit permitting reports                                         | 10 days  | Thu 8/6/26   | Wed 8/19/26  | Scoping & Collapsing of burrows 11/30                     |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 156 |           | Burrowing Owl (FWC) (Nesting Season - July 11th to February 14th) | 43 days  | Tue 11/17/26 | Thu 1/14/27  | Submit Permitting reports 12/3                            |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 157 |           | Scoping & Collapsing of burrows                                   | 10 days  | Tue 11/17/26 | Mon 11/30/26 | FWC Verification of completeness 1/14                     |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 158 |           | Submit Permitting reports                                         | 3 days   | Tue 12/1/26  | Thu 12/3/26  | UTILITIES/EASEMENTS 10/27                                 |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 159 |           | FWC Verification of completeness                                  | 30 days  | Fri 12/4/26  | Thu 1/14/27  | Power 10/27                                               |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 160 |           | UTILITIES/EASEMENTS                                               | 165 days | Wed 3/11/26  | Tue 10/27/26 | Service Extension 10/27                                   |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 161 |           | Power                                                             | 165 days | Wed 3/11/26  | Tue 10/27/26 | Power - Easement Agreement & Depictions / Exhibits 5/12   |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 162 |           | Service Extension                                                 | 165 days | Wed 3/11/26  | Tue 10/27/26 | Telecom - Easement Agreement & Depictions / Exhibits 5/12 |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 163 |           | Agreement                                                         | 45 days  | Wed 3/11/26  | Tue 5/12/26  | PROCUREMENT (General Contractor) 10/28                    |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 164 |           | Extension                                                         | 6 mons   | Wed 5/13/26  | Tue 10/27/26 | Prepare RFP 2/24                                          |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 165 |           | Power - Easement Agreement & Depictions / Exhibits                | 45 days  | Wed 3/11/26  | Tue 5/12/26  | Bidding 3/17                                              |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 166 |           | Telecom - Easement Agreement & Depictions / Exhibits              | 45 days  | Wed 3/11/26  | Tue 5/12/26  | Receive Proposals 3/17                                    |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 167 |           | PROCUREMENT (General Contractor)                                  | 178 days | Fri 2/20/26  | Wed 10/28/26 | Level Proposals 3/31                                      |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 168 |           | Prepare RFP                                                       | 3 days   | Fri 2/20/26  | Tue 2/24/26  | Issue LOI 3/31                                            |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 169 |           | Bidding                                                           | 15 days  | Wed 2/25/26  | Tue 3/17/26  | Draft / Execute Contract 4/7                              |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 170 |           | Receive Proposals                                                 | 0 days   | Tue 3/17/26  | Tue 3/17/26  | Notice of Commencement 10/28                              |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 171 |           | Level Proposals                                                   | 10 days  | Wed 3/18/26  | Tue 3/31/26  | CONSTRUCTION 11/10                                        |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 172 |           | Issue LOI                                                         | 0 days   | Tue 3/31/26  | Tue 3/31/26  | Construction Cycle                                        |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 173 |           | Draft / Execute Contract                                          | 5 days   | Wed 4/1/26   | Tue 4/7/26   | Tenant Access - Fixturing                                 |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 174 |           | Notice of Commencement                                            | 45 edays | Sun 9/13/26  | Wed 10/28/26 | Substantial Completion                                    |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 175 |           | CONSTRUCTION                                                      | 370 days | Wed 10/28/26 | Tue 3/28/28  |                                                           |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 176 |           | Mobilize                                                          | 10 days  | Wed 10/28/26 | Tue 11/10/26 |                                                           |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 177 |           | Construction Cycle                                                | 18 mons  | Wed 11/11/26 | Tue 3/28/28  |                                                           |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 178 |           | Tenant Access - Fixturing                                         | 60 days  | Mon 11/8/27  | Fri 1/28/28  |                                                           |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
| 179 |           | Substantial Completion                                            | 0 days   | Tue 3/28/28  | Tue 3/28/28  |                                                           |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |             |   |   |   |   |   |  |  |  |  |  |  |
